



this is
Redcar & Cleveland



Cowbar Lane Realignment Phase 1 – Detail Design

Steering Group 1 – 17/09/2025

Introduction


- AtkinsRéalis appointed Design Consultant by RCBC
 - › AtkinsRéalis are an international multi disciplinary Design Consultant
 - › Various offices in the North East including Stockton & Newcastle
- Design Lead will be David Shea
 - › Chartered Civil Engineer with over 25 years experience in the construction industry
 - › Undertaken the role of design lead on various highway schemes for both National Highways and Local Authorities. Most recently being involved with a number of new highway projects on Teesworks
 - › Supported by specialist design leads in drainage, geotechnics, pavement, building & street lighting.



Programme


- Key Dates

- › Procure and undertake advance surveys – currently ongoing
- › Commence Detail Design – October 2025
- › Produce Tender Pack – February 2026
- › Contract Award – April 2026
- › Construction Period (estimate) – 8 months

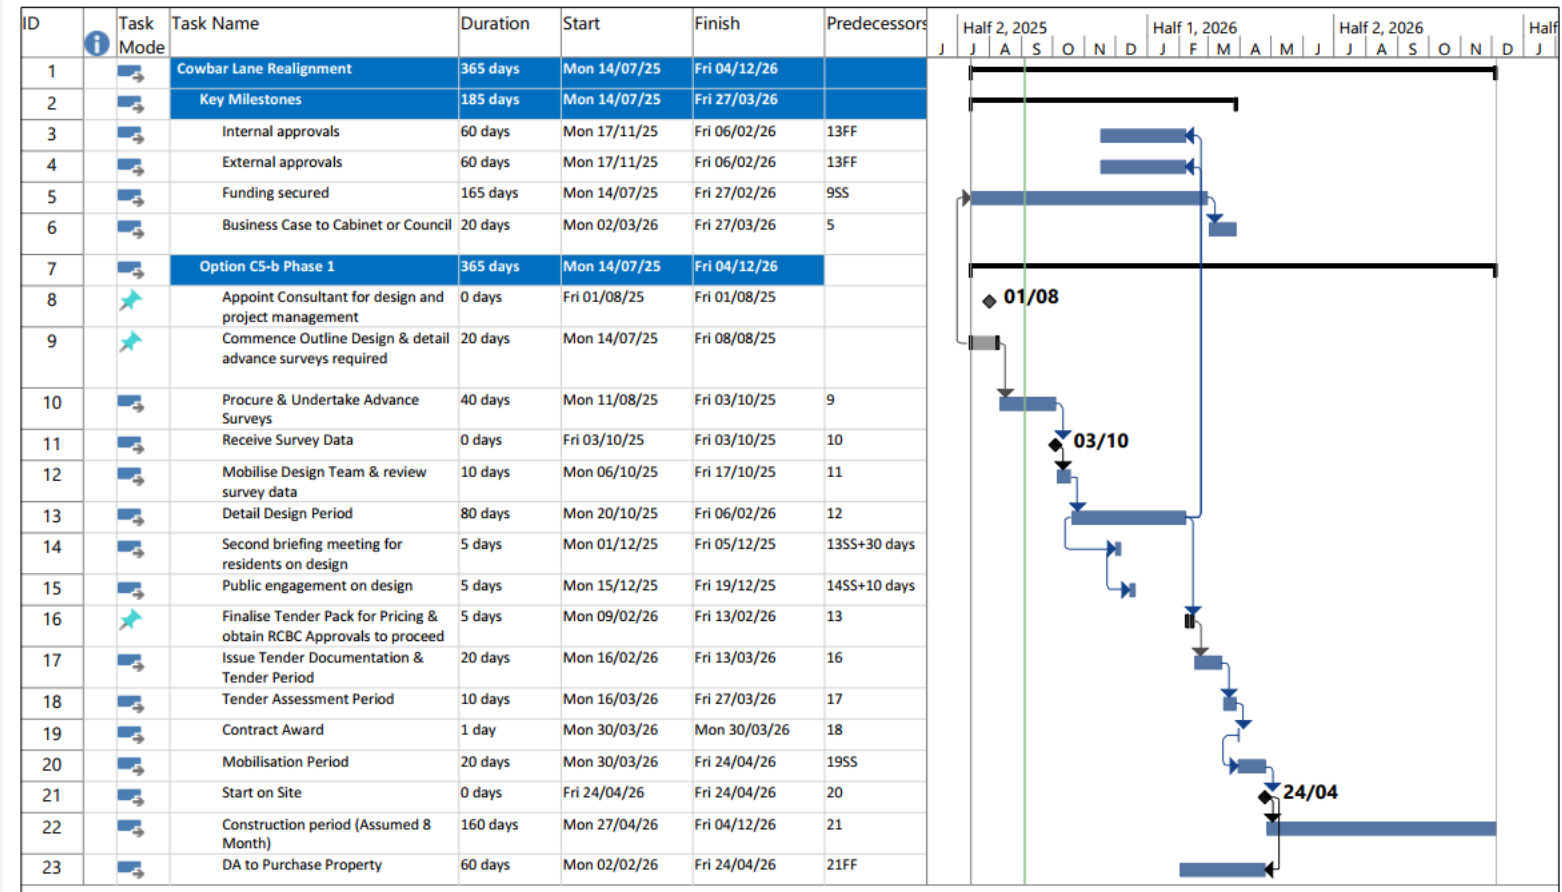


Progress So Far

- Outline design carried out on OS base – Phase 1 Plan

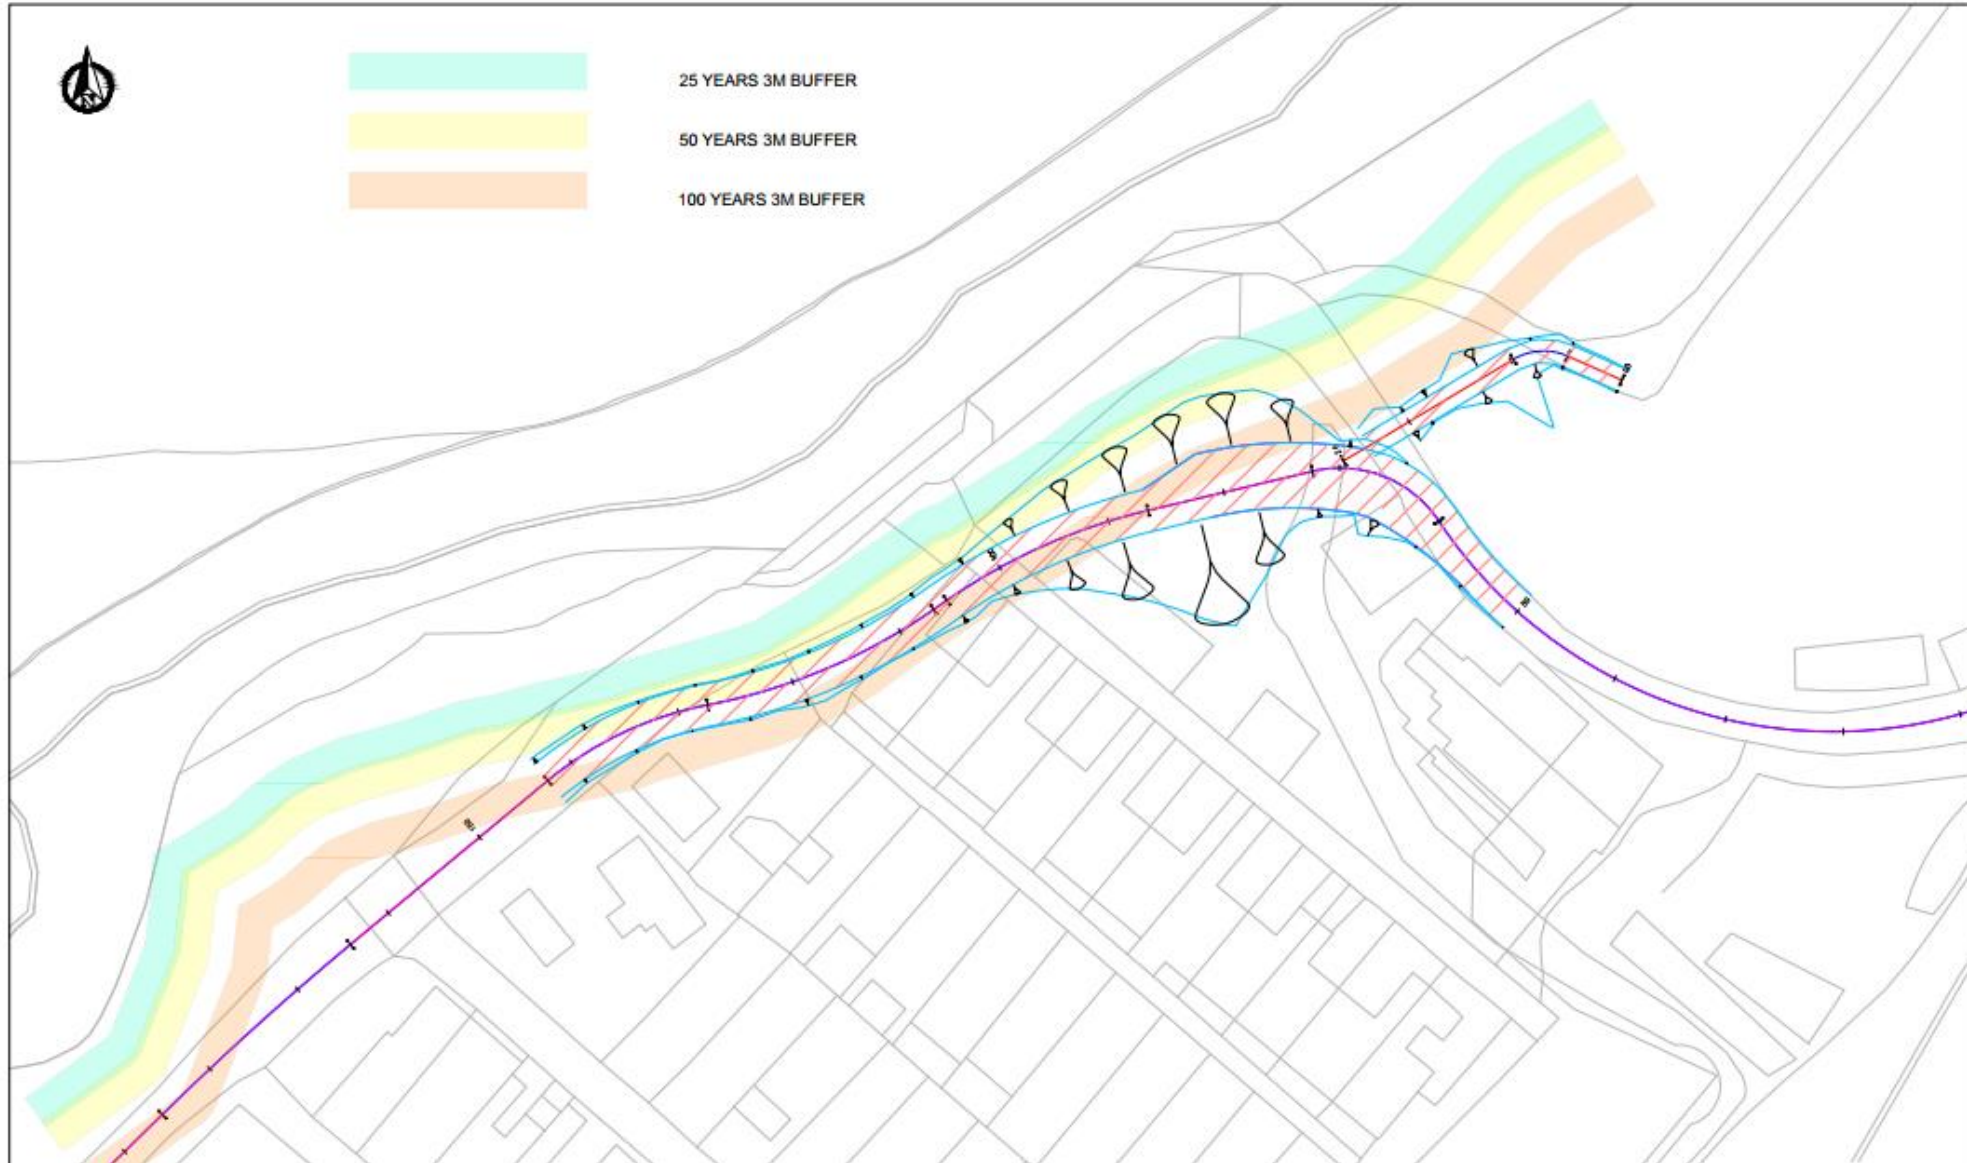


Progress So Far

- Outline design carried out on OS base – Phase 1 Profile

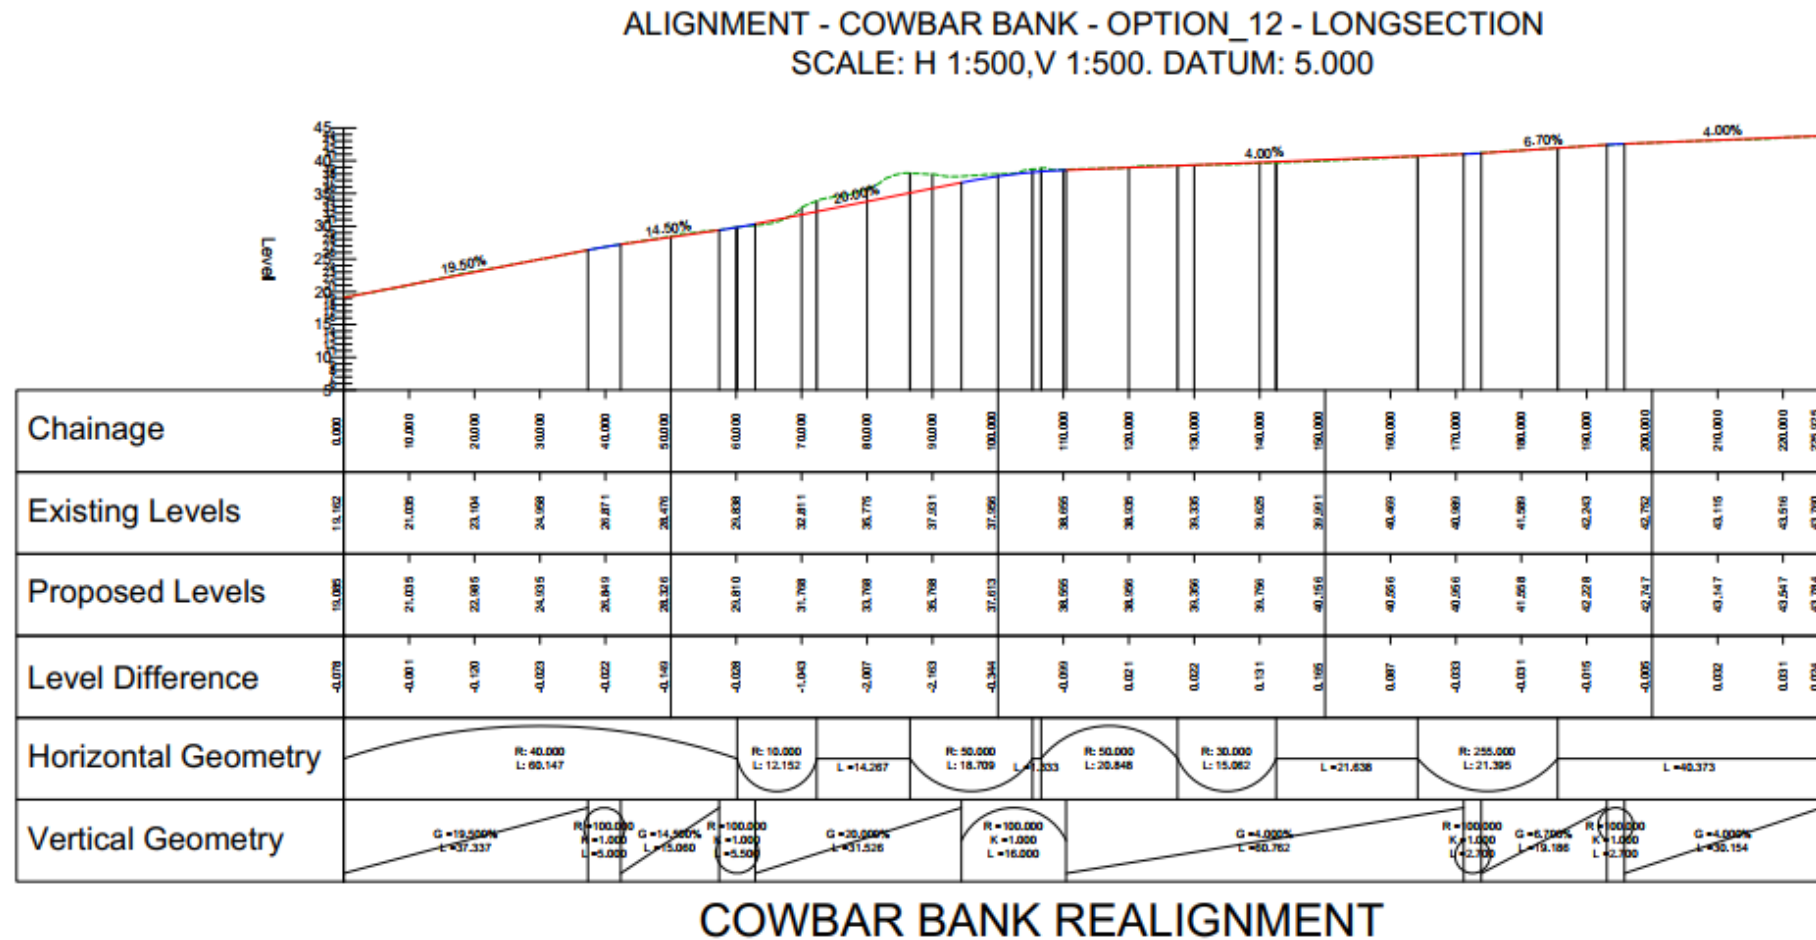


Progress So Far

- Outline design carried out on OS base – Phase 2



Progress So Far

- Outline design carried out on OS base – Phase 3

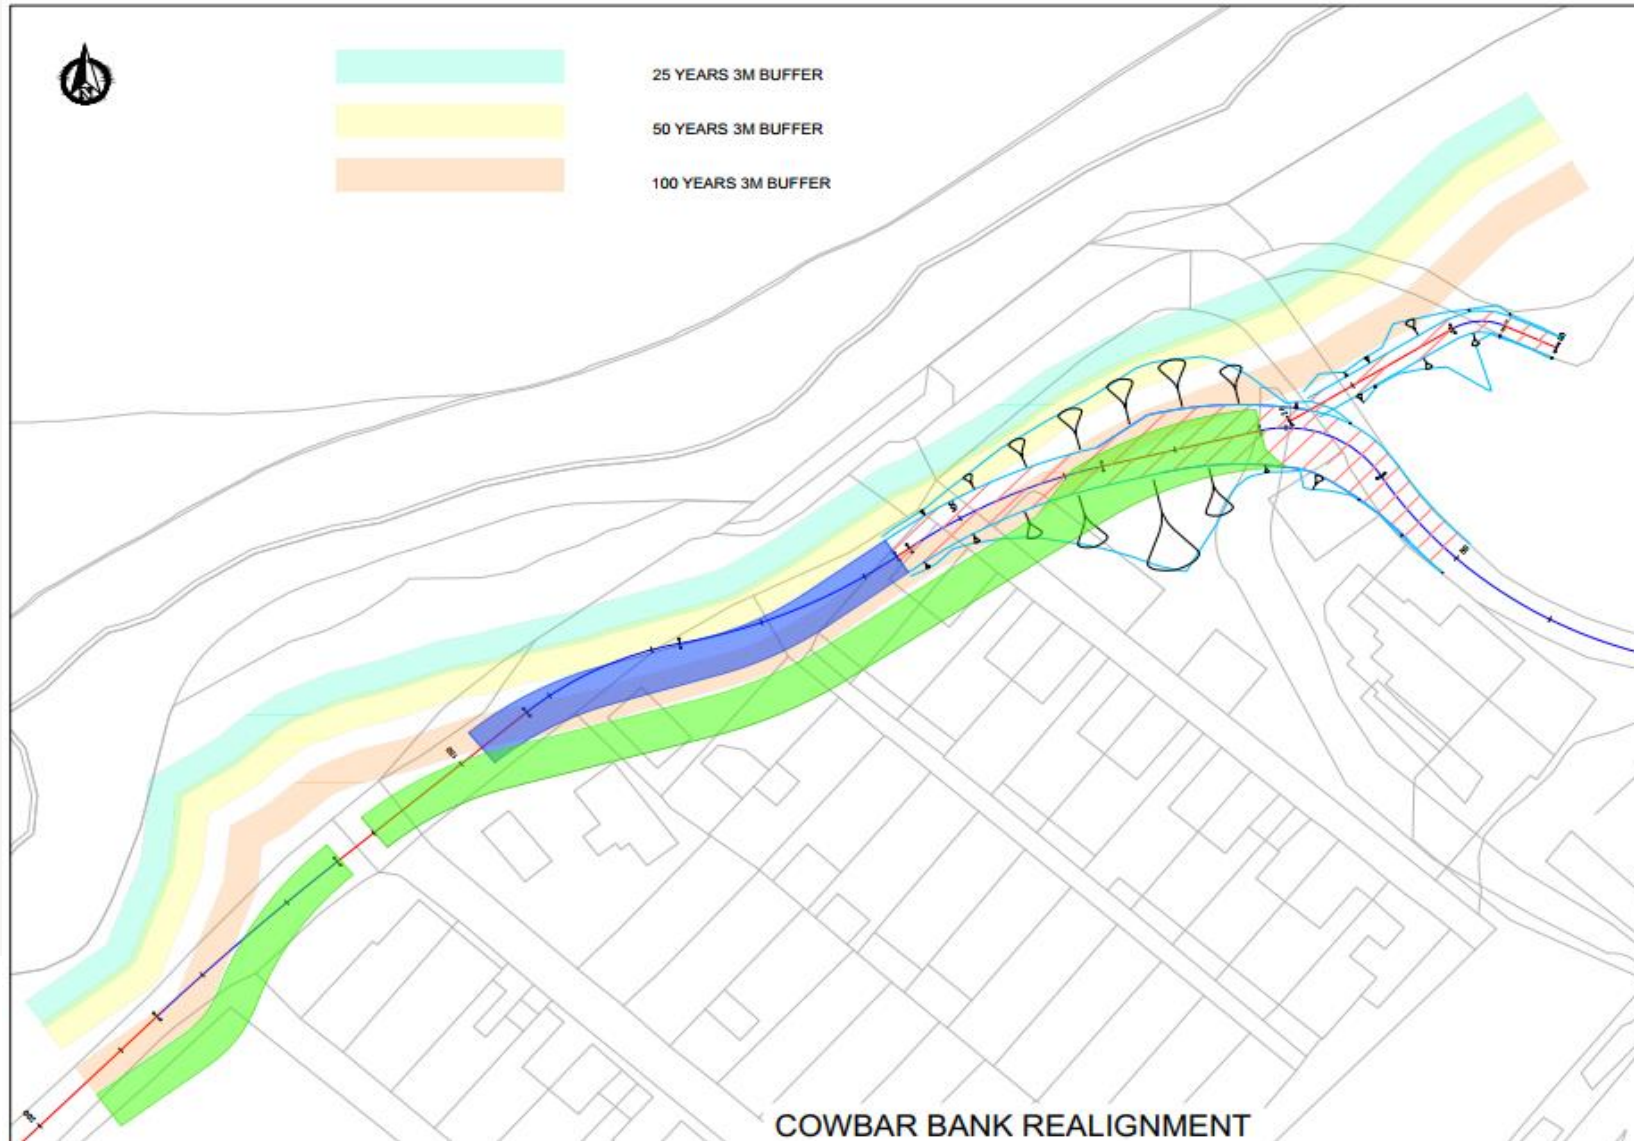

Progress So Far

- Advanced surveys ongoing:
 - › Topographic Survey
 - › Drainage
 - › Utilities
 - › GPR for pile detection
- Previous As-built data found and currently being assessed
- Detail Design will commence on receipt of survey information

